



PRE-BID MEETING SIGN-IN SHEET

Project: CAT / RAMP + Gap

Date and Time: Thursday, August 9, 2018, 10:30 am

City Hall West, 950 West Mall Square, Conference Rm. 156, Alameda, CA 94501

CIP Number: 91402 (P.W. No.: 03-18-11)


	Name:	Agency/Firm:	Phone:	Email:
1	Rochelle Wheeler <input checked="" type="checkbox"/>	Transportation Planning Div., Coordinator	(510) 747-7442	rwheeler@alamedaca.gov
2	Jack Dybas <input checked="" type="checkbox"/>	Alameda Public Works Dept. PM	(510) 747-7948	jdybas@alamedaca.gov
3	Eric Swanson <input checked="" type="checkbox"/>	BKF Engineers (Prime Design Engineer)	(925) 940-2206	eswanson@bkf.com
4	Christine Gurske <input checked="" type="checkbox"/>	BKF Engineers (Prime Design Engineer)	(925) 940-2253	cgurske@bkf.com
5	Jesse Jones <input checked="" type="checkbox"/>	Placeworks (Prime Design Consultant)	(510) 848-3815	jjones@placeworks.com
6	Steve Patterson <input checked="" type="checkbox"/>	Park Engineering (Construction Manager)	(510) 701-0319	spatterson@park-eng.com
7	Victor Early <input checked="" type="checkbox"/>	Tetra Tech (Environmental Consultant)	(510) 302-6332	victor.early@tetrattech.com
8	Ruchil Shah <input type="checkbox"/>	Ninyo & Moore (Testing & Inspections)	(510) 343-3000	rshah@ninyoandmoore.com
9	Su Soe <input checked="" type="checkbox"/>	Ninyo & Moore (Testing & Inspections)	(510) 343-3000 x15215	ssoe@ninyoandmoore.com
10	KEVIN JOHANSON	GORDON N. BALL, INC.	925-838-5675	ESTIMATING@BALLCONC.COM
11	Alejandro Peña	McGuire and Hester	(510) 632-7676	estimating@mcguireandhester.com
12	OCTAVIO JIMENEZ	MCGUIRE and HESTER	(510) 632-7676	estimating@mcguireandhester.com
13	DAVID MOHAMMED	REDGWICK CONSTRUCTION	(510) 792-1727	estimating@redgwick.com
14	HUSSEIN RADHI	Ray's Electric	(510) 577-7700	Hussein@RaysElectric.net
15				
16				
17				

CIP NUMBER: 91402 (P.W. NO.: 03-18-11)

38	Cennor Falk	Hoseley Corp	(415) 404 8997	estimating@hoseley.com
39	Carlos Lopez	Suarez & Munoz Construction	(510) 782-6065	john@suarezmunoz.com carlos@suarezmunoz.com
40	Ziad Nassoura	Gallagher + Burk	925.361.1458	znassoura@gallagherburk.com
41				
42				
43				
44				
45				
46				
47				
48				
49				
50				
51				
52				

Cross Alameda Trail Ralph Appezzato Memorial Parkway Improvements (aka; CAT / RAMP + Gap)

No. P.W. 03-18-11 CIP#: 91402



PROJECT MANUAL INCLUDING:
NOTICE TO CONTRACTORS, INSTRUCTIONS TO BIDDERS, PROPOSAL FORMS, BID
SCHEDULE, GENERAL PROVISIONS, SPECIAL PROVISIONS, ATTACHMENTS, AND
CONTRACT DOCUMENTS

FOR

CROSS ALAMEDA TRAIL
RALPH APPEZZATO MEMORIAL PARKWAY IMPROVEMENTS
(a.k.a. CAT/RAMP+GAP)
ALONG ATLANTIC AVENUE BETWEEN
MAIN STREET AND CONSTITUTION WAY

CIP# 91402, P.W. 03-18-11

LOCATED IN

CITY OF ALAMEDA - ALAMEDA COUNTY - CALIFORNIA

JULY 2018

DEPARTMENT OF PUBLIC WORKS
CITY OF ALAMEDA
950 WEST MALL SQUARE
ALAMEDA, CA 94501

BID DOCUMENTS

CB-16-0427

O.P.A.M.P.

RECEIVED
JUL 19 2018
PERMIT CENTER
ALAMEDA, CA 94501

Pre-Bid Meeting

Thursday, August 9, 10:30 am
City of Alameda City Hall West
Public Works Department
950 West Mall Square
Conference Room 156

Thursday, August 9, 2018

Agenda

- ❑ **Sign in Sheet & Introductions**
- ❑ **Scope of Work**
- ❑ **Engineer's Estimate:** \$3,430,000
- ❑ **View or Download Bidding Documents:** BPXpress Reprographics,
www.blueprintexpress.com/alameda, “Find Jobs to Bid”, “City of Alameda” or call (510) 559-8299,
or email Richmond@blueprintexpress.com.
- ❑ **Bid Advertisement:** Thursday, August 2, 2018
- ❑ **Bid Questions Cut-Off Date:** Wednesday, August 22, 2018
- ❑ **Responses to Final Bid Questions:** by Thursday, August 23, 2018.
- ❑ **Bid Opening:** Thursday, August 30, 2018,
- ❑ **City Council Award:** Tuesday, October 16, 2018
- ❑ **Contract Time:** One Hundred forty-six (146) working days
from Notice to Proceed
- ❑ **Q & A?**

Sign In Sheet



PRE-BID MEETING SIGN-IN SHEET

Project: CAT / RAMP + Gap

Date and Time: Thursday, August 9, 2018, 10:30 am


City Hall West, 950 West Mall Square, Conference Rm. 156, Alameda, CA 94501

CIP Number: 91402 (P.W. No.: 03-18-11)

	Name:		Agency/Firm:	Phone:	Email:
1	Rochelle Wheeler	<input type="checkbox"/>	Transportation Planning Div., Coordinator	(510) 747-7442	rwheeler@alamedaca.gov
2	Jack Dybas	<input checked="" type="checkbox"/>	Alameda Public Works Dept. PM	(510) 747-7948	jdybas@alamedaca.gov
3	Eric Swanson	<input type="checkbox"/>	BKF Engineers (Prime Design Engineer)	(925) 940-2206	eswanson@bkf.com
4	Christine Gurske	<input type="checkbox"/>	BKF Engineers (Prime Design Engineer)	(925) 940-2253	cgurske@bkf.com
5	Jesse Jones	<input type="checkbox"/>	Placeworks (Prime Design Consultant)	(510) 848-3815	jjones@placeworks.com
6	Steve Patterson	<input type="checkbox"/>	Park Engineering (Construction Manager)	(510) 701-0319	spatterson@park-eng.com
7	Victor Early	<input type="checkbox"/>	Tetra Tech (Environmental Consultant)	(510) 302-6332	victor.early@tetrattech.com
8	Ruchil Shah	<input type="checkbox"/>	Ninyo & Moore (Testing & Inspections)	(510) 343-3000	rshah@ninyoandmoore.com
9	Su Soe	<input type="checkbox"/>	Ninyo & Moore (Testing & Inspections)	(510) 343-3000 x15215	ssoe@ninyoandmoore.com
10					
11					
12					
13					
14					

CAT / RAMP + Gap Scope of Work

PROJECT LOCATION

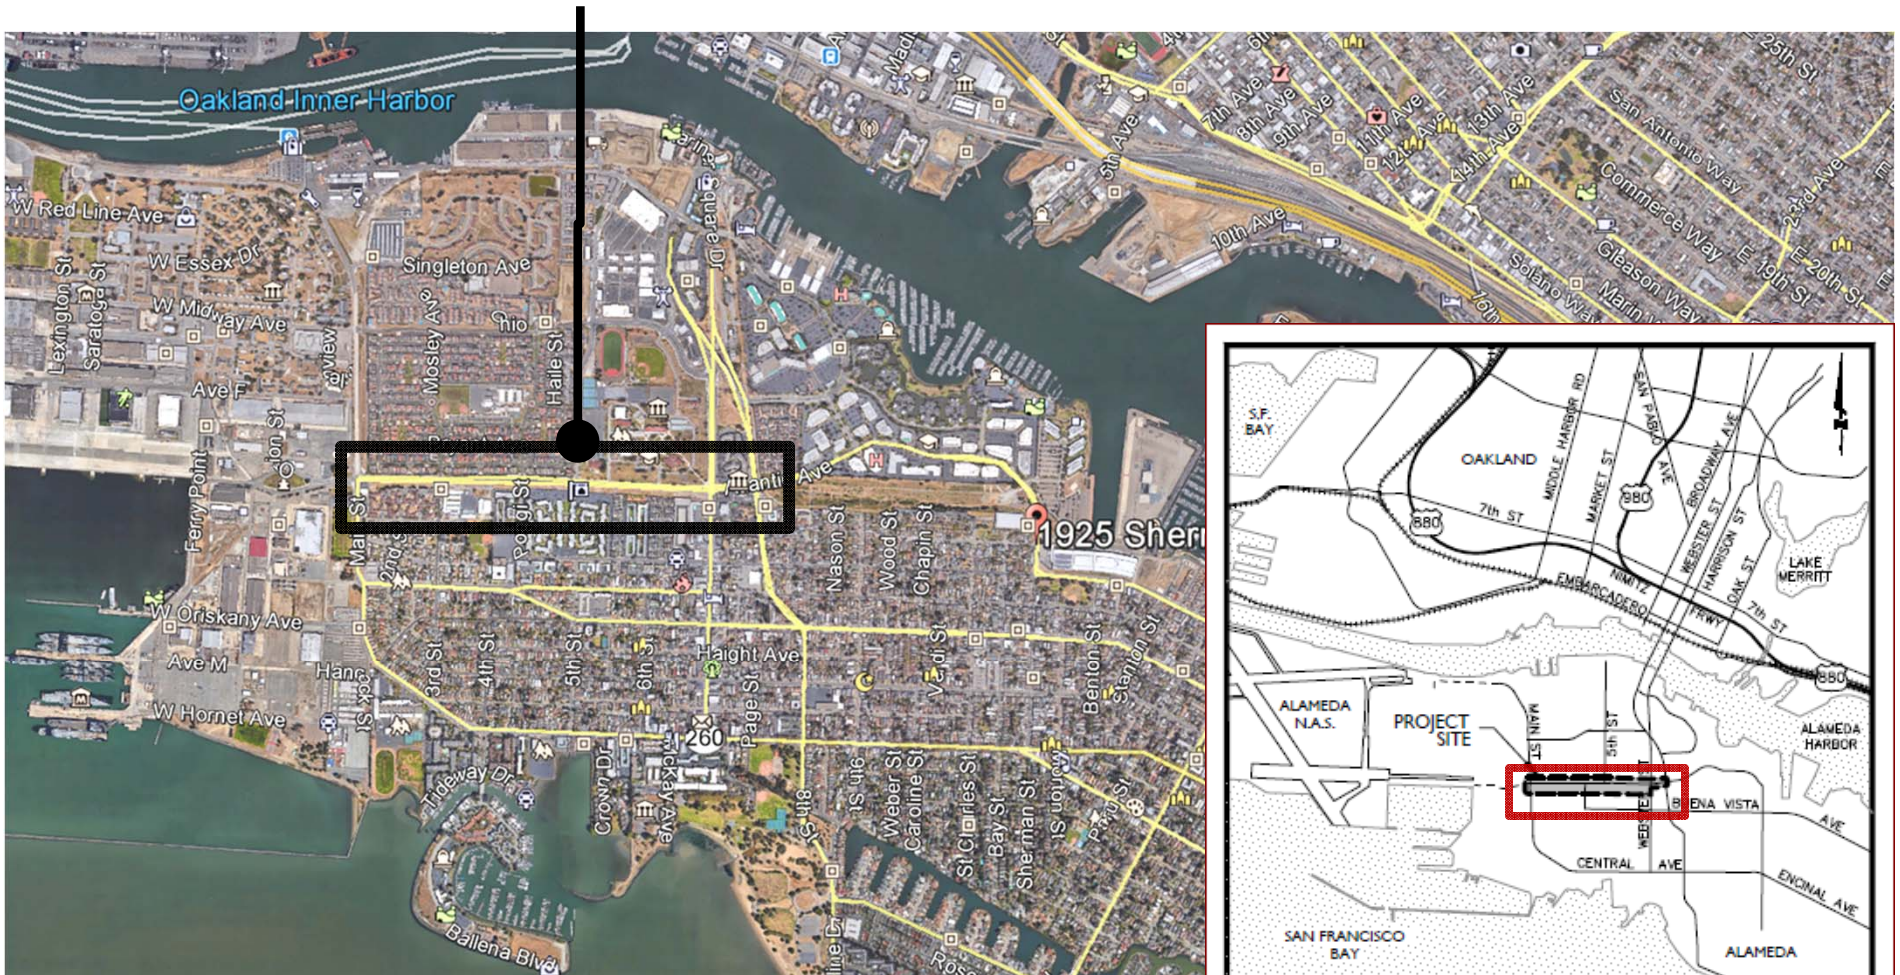

LOCATION MAP
NTS




CAT / RAMP + Gap Scope of Work

This Project is part of the City's larger Cross Alameda Trail (CAT) project, a premiere crosstown, bicycling and walking corridor that when complete will connect the west side of the island to the east, from the former Naval Air Base to the Miller-Sweeney (Fruitvale) Bridge.

The CAT is being constructed in segments. The CAT/RAMP + Gap segment, running parallel to and south of Ralph Appezzato Municipal Parkway, between Main Street and Constitution Way is approximately 0.9 miles in length, and is composed of two sub-segments:

1. Ralph Appezzato Memorial Parkway (Main Street to Webster Street)
2. Atlantic Avenue (Webster Street to Constitution Way)

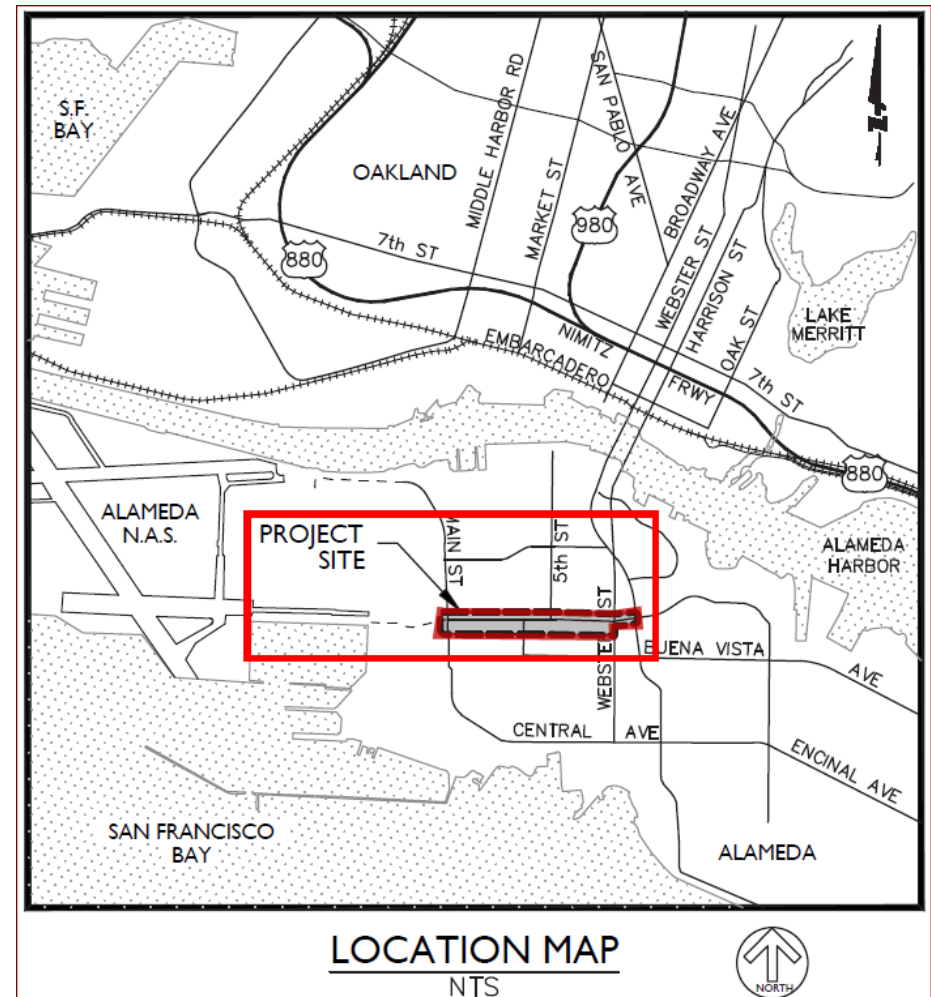


CAT / RAMP + Gap Scope of Work

1. Ralph Appezato Memorial Parkway (Main Street to Webster Street; 'CAT / RAMP')

Construction of walking and bicycling paths, plus a jogging path, in the City-owned abandoned railroad right-of-way. Approximately 70 foot wide right-of-way, immediately to the south of Appezato Parkway, adjacent to apartment complexes, schools, several businesses and a Boys and Girls Club. This segment includes the following additional features:

- Connector trails to intersecting streets; Fifth Street and West Campus Drive,
- Pedestrian, bicycle, and ADA improvements, w/ signage at intersecting streets,
- Hardscaped, landscaped plazas at each end; Main Street and Webster Street,
- Trees, shrubs, bioretention and self-retaining areas, w/ landscaping and urban runoff control, and
- Traffic signal modifications at Fifth Street, Webster St., and Constitution Way,

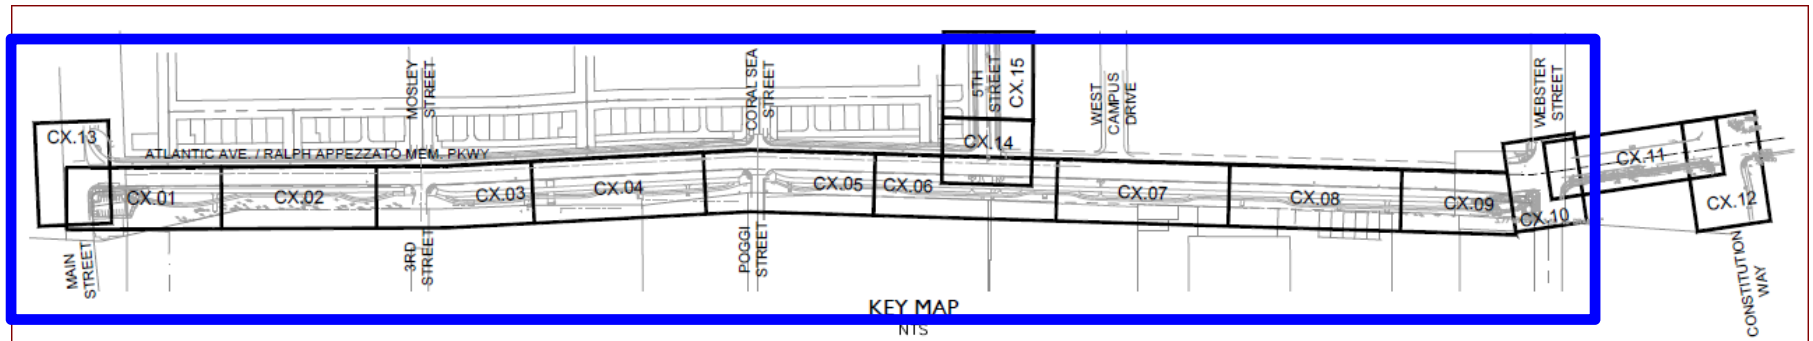

OVERALL SITE PLAN


Note: This segment includes significant earthwork in the excavation (relocation and 'capping') of contaminated soils, creating the subgrade for the bicycle and pedestrian paths, with the placement of a soil cap over the majority of the site.

(exhibit from CAT / RAMP + Gap Plans)

CAT / RAMP + Gap Scope of Work

2. Atlantic Avenue (Webster Street to Constitution Way; 'Gap')


Construction of two-way bicycle lanes on the south side of this short urban block, one half of which will be at sidewalk-grade (west of business parking lot driveway), and the other at street-grade (east of this driveway). This CAT section includes improvements to the two intersections, the busiest in the City, to facilitate safe pedestrian and bicycle crossings. Project includes signal modifications, plus installation of a mid-block crossing with a flashing beacon, and the creation of a new bus stop platform.

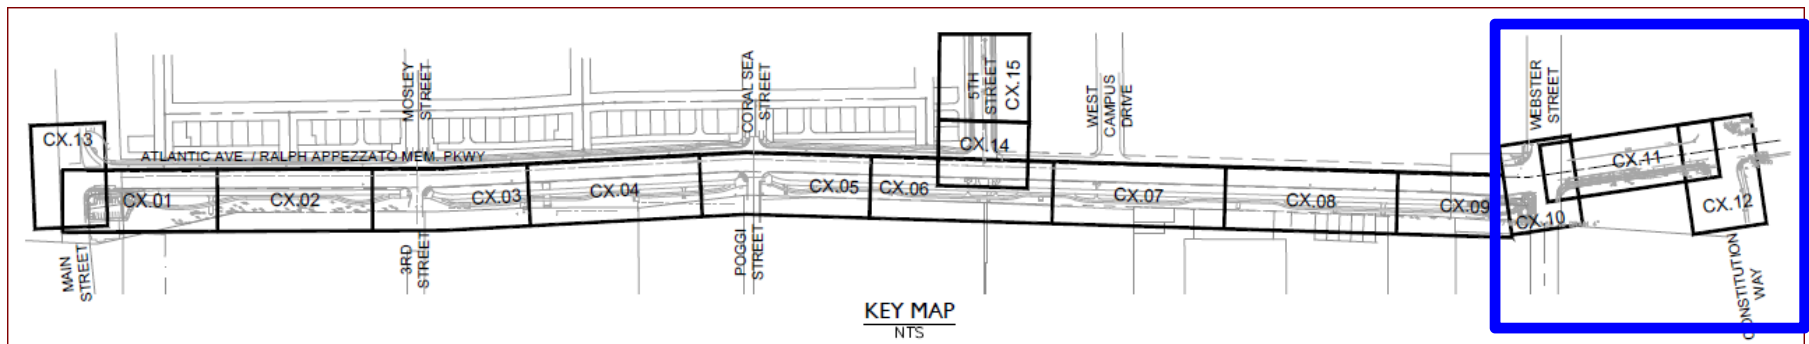

OVERALL SITE PLAN

(exhibit from CAT / RAMP + Gap Plans)


CAT / RAMP + Gap Scope of Work

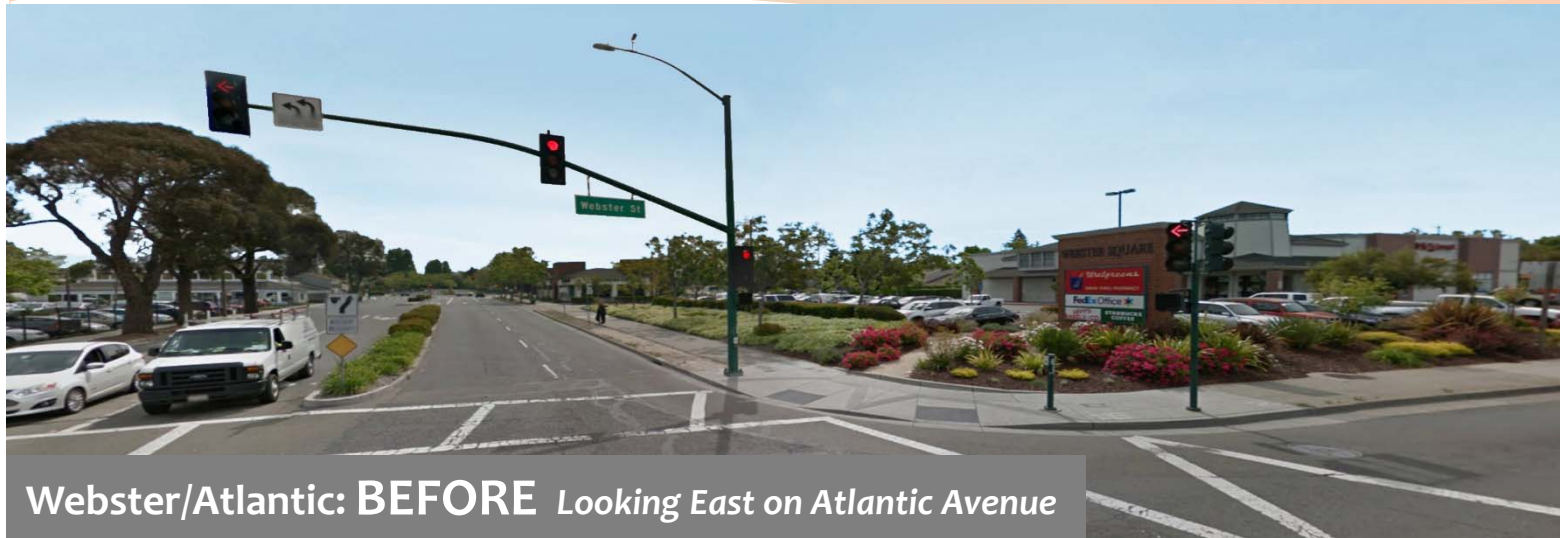

CAT / RAMP + Gap Scope of Work

The Project's current funding sources are:

- FTA (Federal Transit Administration (via BART)) earmark,
- Alameda CTC Countywide Discretionary Grant (sales tax and vehicle registration fees),
- Transportation Development Act, Article 3,
- CDBG (Community Development Block Grant (Federal)),
- Transportation Fund for Clean Air (TFCA) Bikeways Fund (BAAQMD).

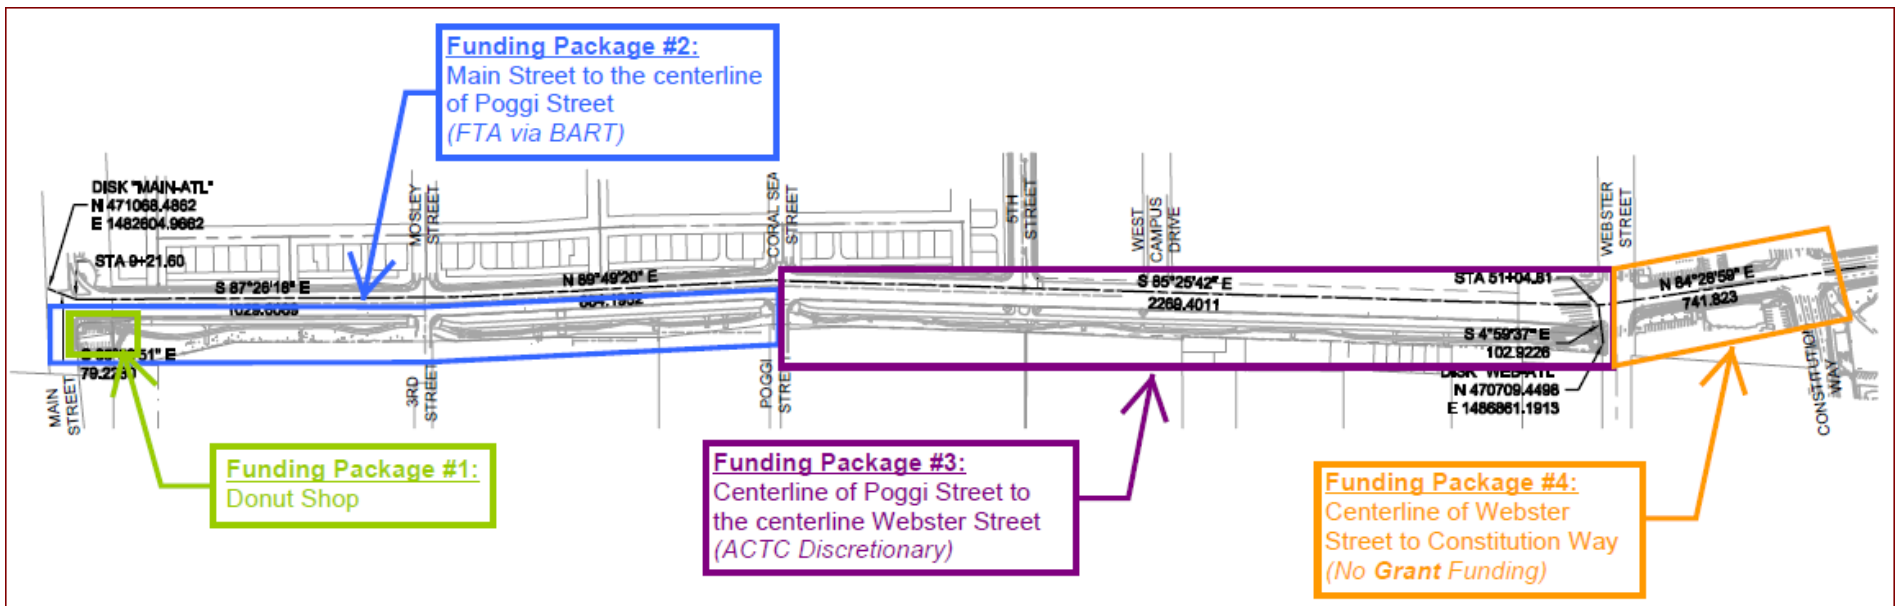

ATTACHMENT P – CAT RAMP FUNDING PACKAGE EXHIBIT

(exhibit from CAT / RAMP + Gap Project Manual)


CAT / RAMP + Gap Scope of Work

ATTACHMENT M – SOIL REMEDIATION DOCUMENTS

The following documents will be made available as part of the Bid Package and can be found at the following location under “*Site Maps/Documents*”:

http://geotracker.waterboards.ca.gov/profile_report?global_id=T10000006774

- “Draft Soil Remediation Workplan for the Cross Alameda Trail”, April 14, 2017
- “Investigation Report and RAP for the Cross Alameda Trail”, September 2016
- “Investigation and Risk Assessment Report for the Cross Alameda Trail”, October 2015



Draft


Soil Remediation Workplan for the Cross Alameda Trail

City of Alameda
Department of Public Works
Alameda, California

April 14, 2017

Prepared for:
City of Alameda
Department of Public Works
Alameda, California

Prepared by:
Tetra Tech, Inc.
1999 Harrison Street, Suite 500
Oakland, California 94612
510-302-6300




Draft

Investigation Report for the Cross Alameda Trail


City of Alameda
Department of Public Works
Alameda, California

September 2016

Prepared for:
City of Alameda
Department of Public Works
Alameda, California



Prepared by:
Tetra Tech, Inc.
1999 Harrison Street, Suite 500
Oakland, California 94612
510-302-6300




Draft

Investigation and Risk Assessment Report for the Cross Alameda Trail

City of Alameda
Department of Public Works
Alameda, California

October 2015

Prepared for:
City of Alameda
Department of Public Works
Alameda, California



Prepared by:
Tetra Tech, Inc.
1999 Harrison Street, Suite 500
Oakland, California 94612
510-302-6300

(exhibit from CAT / RAMP + Gap Project Manual)

CAT / RAMP + Gap Scope of Work

SCOPE OF WORK ALSO INCLUDES ...

AGREEMENT TO BE BOUND TO PSA

PROJECT STABILIZATION AGREEMENT FOR THE CITY OF ALAMEDA

The undersigned party confirms that it agrees to be bound by the City of Alameda Project Stabilization Agreement A copy of the Agreement is included as **ATTACHMENT 'J'**.

CROSS ALAMEDA TRAIL
RALPH APPEZZATO MEMORIAL PARKWAY IMPROVEMENTS

AGREEMENT TO BE BOUND TO PSA

PROJECT STABILIZATION AGREEMENT FOR THE CITY OF ALAMEDA AGREEMENT TO BE BOUND

The undersigned party confirms that it agrees and assents to comply with and to be bound by the City of Alameda Project Stabilization Agreement as such Agreement may, from time to time, be amended by the parties or interpreted pursuant to its terms. A copy of the Agreement is included as Attachment K.

By executing this Agreement To Be Bound, the undersigned party subscribes to, adopts and agrees to be bound by the written terms of the legally established trust agreements, as set forth in section 17, specifying the detailed basis upon which contributions are to be made into, and benefits made out of, such Trust Fund(s) and ratifies and accepts the trustees appointed by the parties to such Trust Fund(s) and agrees to execute a separate Subscription Agreement(s) for Trust Funds when such Trust Fund(s) require(s) such document(s).

Such assent and obligation to comply with and to be bound by this Agreement shall extend to all work covered by said Agreement undertaken by the undersigned party. The undersigned party shall require all of its subcontractors, of whatever tier, to become similarly bound for all their work within the scope of this Agreement by signing an identical Agreement To Be Bound.

This letter shall constitute a subscription agreement, to the extent of the terms of the letter.

Dated: _____ Project: _____

Signature of Authorized Officer

Authorized Officer & Title

Name of Contractor/Employer(s)

Contractor/Employer(s) Address

CSLB #

Area Code Phone

E-mail and/or Fax

Motor Carrier (CA) Permit Number

DIR Prevailing Wage Registration #

(exhibit from CAT / RAMP + Gap Project Manual)

Engineer's Estimate

CITY OF ALAMEDA
CROSS ALAMEDA TRAIL - RALPH APPEZZATO MEMORIAL PARKWAY + GAP
BASE BID SCHEDULE

ITEM	DESCRIPTION	SPEC. REF.	UNIT COST	QTY.	UNIT	AMOUNT
FUNDING PACKAGE #1 (Donut Shop)						
1	REMOVE CONCRETE CURB	10.19		39	LF	\$
2	ACCESSIBLE RAMPS	10.44		100	SF	\$
3	ACCESSIBLE SIGN	10.65		1	EA	\$
4	AC PAVEMENT GRIND	10.46		3,225	SF	\$
5	AC PAVEMENT OVERLAY	10.46		39	TON	\$
6	8" CONCRETE CURB	10.44		39	LF	\$
7	INSTALL PARKING STRIPING (4")	10.46		370	SF	\$
FUNDING PACKAGE #2 (FTA via BART)						
8	MOBILIZATION (2.5% of Base Bid)	10.04		1	LS	\$
9						
10						
11	INSTALL PROJECT SIGNS	10.06		1	LS	\$
12	CONSTRUCTION STAKING	10.34		1	LS	\$
13	CONSTRUCTION SURVEYING (CAP VERIFICATION)	10.30		1	LS	\$
14	SWPPP/EROSION CONTROL	10.08		1	LS	\$
15	CLEARING AND GRUBBING	10.16		117,868	SF	\$
16	TREE REMOVAL	10.18		29	EA	\$
17	TREE TRIMMING	10.18		1	LS	\$
18	REMOVE CONCRETE CURB AND GUTTER	10.19		508	LF	\$
19	REMOVE CONCRETE PAVING	10.19		2,874	SF	\$
20	REMOVE ASPHALT CONCRETE PAVING	10.19		14,594	SF	\$
21	SALVAGE SIGNS	10.16		2	EA	\$
22	TREE PROTECTION	10.18		1	LS	\$
23	REMOVE BOLLARDS	10.21		6	EA	\$
24	REMOVE AND DISPOSE OF EXISTING BUILDING	10.20		1	EA	\$
25	REMOVE CHAIN LINK FENCE	10.22		150	LF	\$
26	TEMPORARY CONTAINMENT	10.27		1,480	CY	\$
27	GEOTEXTILE SEPARATION BARRIER	10.33		155,719	SF	\$
28	REUSE EXISTING MULCH	10.56		20,400	SF	\$
29	EROSION CONTROL LAYER / HYDROSEED	10.53		81,600	SF	\$

CAT/RAMP + GAP
CIP# 91402

BID SCHEDULE
Page xx

ITEM	DESCRIPTION	SPEC. REF.	UNIT COST	QTY.	UNIT	AMOUNT
30	EARTHWORK - EXCAVATION (CUT TO BURIAL)	10.32		3,230	CY	\$
31	FULL DEPTH RECLAMATION (REVOCABLE)	10.31		59,700	SF	\$
32	FINE GRADING	10.29		59,700	SF	\$
33	CEMENT APPLICATION (REVOCABLE)	10.31		20	TON	\$
34	IMPORT AND PLACE CLEAN FILL (REVOCABLE)	10.28		9,600	CY	\$
35	CLASS II RECYCLED AGGREGATE BASE - 8" BIKE & JOG, 4" WALKING	10.45		2,000	TON	\$
36	WALKING PATH - 2" ASPHALT	10.46		125	TON	\$
37	JOGGING PATH - 4" DECOMPOSED GRANITE	10.47		203	TON	\$
38	3" ASPHALT AT INTERSECTIONS	10.46		50	TON	\$
39	CONCRETE PAVING (PLAZAS)	10.44		3,100	SF	\$
40	4" CONCRETE AT INTERSECTIONS & ACCESS PATHS	10.44		3,635	SF	\$
41	BICYCLE PATH - 3" ASPHALT	10.46		435	TON	\$

The Engineer's Base Bid Estimate for this project is \$3,430,000.

ITEM	DESCRIPTION	SPEC. REF.	UNIT COST	QTY.	UNIT	AMOUNT
42	(WAY)					
45	BICYCLE CURB RAMP	10.44		457	SF	\$
46	CONCRETE CURB AND GUTTER	10.44		813	LF	\$
47	MAIN STREET DRIVEWAY	10.44		1	EA	\$
48	STRIPING: 12" SOLID WHITE LINE	10.48		30	LF	\$
49	STRIPING: 4" SOLID YELLOW	10.48		400	LF	\$
50	STRIPING: 4" SOLID WHITE	10.48		120	LF	\$
51	STRIPING: 4" BROKEN YELLOW	10.48		1,350	LF	\$
52	PAVEMENT MARKINGS	10.48		55	EA	\$
53	NEW SIGNAGE	10.65		26	EA	\$
54	LANDSCAPE SOIL PREPARATION (INCLUDES COMPOST AT 6CY/1000SF AT \$1,800/SF)	10.58		551	CY	\$
55	TREE - 15 GALLON	10.59		61	EA	\$
56	CONCRETE BAND	10.44		20	LF	\$
57	PAVERS AT EMERGENCY ACCESS	10.61		475	SF	\$
58	BRICK PAVERS - MORTAR SET WITH CONCRETE BASE	10.62		209	SF	\$
59	BOULDER	10.64		50	TON	\$
60	TRAFFIC SIGNS/POSTS/WAYFINDING SIGNAGE-NOT SHOWN IN PLANS	10.65		1	EA	\$
61	SHEET MULCH (2 LAYERS OF RECYCLED CARDBOARD)	10.67		10,400	SF	\$
62	RECYCLED WOOD MULCH (2 INCH DEPTH/10,400 SF)/REVOCABLE)	10.68		64	CY	\$

CAT/RAMP + GAP
CIP# 91402

BID SCHEDULE
Page xx

BID SCHEDULE

(exhibit from CAT / RAMP + Gap Project Manual

Bid Schedule

ITEM	DESCRIPTION	SPEC. REF.	UNIT COST	QTY.	UNIT	AMOUNT
63	METAL HEADER	10.63		40	LF	\$
64	BENCHES	10.70		3	EA	\$
65	BIKE RACKS	10.72		2	EA	\$
66	TREE GRATE	10.74		1	EA	\$
67	LANDSCAPE MAINTENANCE (1 YEAR)	10.73		1	LS	\$
68	SLOW RELEASE WATERING BAG - TREES	10.52		122	EA	\$
69	ADJUST MANHOLE LID (SS/SD) TO GRADE	10.38		6	EA	\$
70	CONNECT TO EXISTING STORM SYSTEM	10.35		16	EA	\$
71	STORM DRAIN AREA DRAIN	10.36		25	EA	\$
72	SOLID DRAIN LINE, 6" PVC	10.37		576	LF	\$
73	TRAFFIC SIGNAL MODIFICATION (THIRD ST/RAMP)	10.50		1	LS	\$
74	TRAFFIC SIGNAL MODIFICATION (POGGI ST/RAMP)	10.50		1	LS	\$
FUNDING PACKAGE #3 (ACTC Discretionary)						
75	MOBILIZATION (2.5% of Base Bid)	10.04		1	LS	\$
76	TRAFFIC CONTROL	10.04		1	LS	\$
77	TEMPORARY CONSTRUCTION FENCING	10.05		2,429	LF	\$
78	INSTALL PROJECT SIGNS	10.06		1	LS	\$
79	CONSTRUCTION STAKING	10.34		1	LS	\$
80	CONSTRUCTION SURVEYING (CAP VERIFICATION)	10.30		1	LS	\$
81	SWPPP/EROSION CONTROL	10.08		1	LS	\$
82	CLEARING AND GRUBBING	10.16		149,388	SF	\$
83	TREE REMOVAL	10.18		3	EA	\$
84	REMOVE CONCRETE CURB AND GUTTER	10.19		450	LF	\$
85	REMOVE CONCRETE PAVING	10.19		2,985	SF	\$
86	REMOVE ASPHALT CONCRETE PAVING	10.19		6,732	SF	\$
87	SALVAGE SIGNS	10.16		8	EA	\$
88	REMOVE BOLLARDS	10.21		18	EA	\$
89	DEMOLISH EXISTING LIGHT POLE BASES & CAP ELECTRICAL	10.23		1	LS	\$
90	TEMPORARY CONTAINMENT	10.27		1,480	CY	\$
91	GEOTEXTILE SEPARATION BARRIER	10.33		143,740	SF	\$
92	REUSE EXISTING MULCH	10.54		21,100	SF	\$
93	EROSION CONTROL LAYER / HYDROSEED	10.53		84,410	SF	\$
94	EARTHWORK - EXCAVATION (CUT TO BURIAL)	10.32		2,200	CY	\$

CAT/RAMP + GAP
CIP# 91402

BID SCHEDULE
Page xx

ITEM	DESCRIPTION	SPEC. REF.	UNIT COST	QTY.	UNIT	AMOUNT
95	FULL DEPTH RECLAMATION (REVOCABLE)	10.31		56,800	SF	\$
96	FINE GRADING	10.29		56,800	SF	\$
97	CEMENT APPLICATION (REVOCABLE)	10.31		20	TON	\$
98	IMPORT AND PLACE CLEAN FILL (REVOCABLE)	10.28		3,400	CY	\$
99	CLASS II RECYCLED AGGREGATE BASE - 8" BIKE & JOG, 4" WALKING	10.45		2,450	TON	\$
100	WALKING PATH - 2" ASPHALT	10.46		160	TON	\$
101	JOGGING PATH - 4" DECOMPOSED GRANITE	10.47		262	TON	\$
102	3" ASPHALT AT INTERSECTIONS	10.46		11	TON	\$
103	CONCRETE PAVING (PLAZAS)	10.44		5,500	SF	\$
104	4" CONCRETE AT INTERSECTIONS & ACCESS PATHS	10.44		7,275	SF	\$
105	BICYCLE PATH - 3" ASPHALT	10.46		580	TON	\$
106	AGGREGATE BASE SERVICE ROAD FOR MH ACCESS	10.45		90	TON	\$
107	PEDESTRIAN CURB RAMP	10.44		310	SF	\$
108	2" by 4" CDF CAP (INSTALLED ADJACENT TO TRAVEL WAY)			55	CY	\$
109	BICYCLE CURB RAMP	10.44		254	SF	\$
110	CONCRETE CURB AND GUTTER	10.48		88	LF	\$
111	STRIPING: 12" SOLID WHITE LINE	10.48		120	LF	\$
112	STRIPING: 4" SOLID YELLOW	10.48		567	LF	\$
113	STRIPING: 4" SOLID WHITE	10.48		660	LF	\$
114	STRIPING: 4" BROKEN YELLOW	10.48		1,440	LF	\$
115	STRIPING: 6" DOTTED WHITE	10.48		300	LF	\$
116	STRIPING: 6" SOLID WHITE LINE	10.48		1,200	LF	\$
117	PAVEMENT MARKINGS	10.48		101	EA	\$
118	NEW SIGNAGE	10.65		29	EA	\$
119	GREEN THERMOPLASTIC PAVEMENT MARKING	10.48		240	SF	\$
120	IRRIGATION (WEBSTER PLAZA)	10.58		1	LS	\$
121	LANDSCAPE SOIL PREPARATION (INCLUDES COMPOST AT 6CY/1000SF AT 95,200 SF)	10.59		571	CY	\$
122	SHRUBS 1 GALLON	10.59		538	EA	\$
123	TREE - 15 Gallon	10.60		71	EA	\$
124	CONCRETE SEAT WALLS	10.49		37	CY	\$
125	CONCRETE BAND	10.62		56	LF	\$
126	BRICK PAVERS - SAND SET	10.62		545	SF	\$
127	BRICK PAVERS - MORTAR SET WITH CONCRETE BASE	10.62		415	SF	\$

CAT/RAMP + GAP
CIP# 91402

BID SCHEDULE
Page xx

(exhibit from CAT / RAMP + Gap Project Manual

Bid Schedule

ITEM	DESCRIPTION	SPEC. REF.	UNIT COST	QTY.	UNIT	AMOUNT
180	TEMPORARY CONSTRUCTION FENCING	10.05		1,028	LF	\$
181	INSTALL PROJECT SIGNS	10.06		1	LS	\$
182	CONSTRUCTION STAKING	10.34		1	LS	\$
183	EROSION CONTROL LAYER / HYDROSEED	10.53		275	SF	\$
184	CLEARING AND GRUBBING (LANDSCAPE)	10.16		580	SF	\$
185	REMOVE CONCRETE CURB AND GUTTER	10.19		440	LF	\$
186	REMOVE CONCRETE CURB (MEDIAN)	10.19		1,850	SF	\$
187	REMOVE ASPHALT CONCRETE PAVING	10.19		2,305	SF	\$
188	REMOVE STRIPING	10.17		1	LS	\$
189	SALVAGE NEWSSTAND	10.26		1	LS	\$
170	TREE REMOVAL	10.18		2	EA	\$
171	TREE PROTECTION	10.18		1	LS	\$
172	RELOCATE IRRIGATION SYSTEM	10.51		1	LS	\$
173	REPLACE AC ROAD SECTION (12" ASPHALT)	10.46		50	TON	\$
174	NEW CONCRETE SIDEWALK	10.44		3,895	SF	\$
175	CONCRETE MEDIAN (ROADWAY MEDIAN)	10.44		175	SF	\$
176	RETAINING CURB	10.44		320	LF	\$
177	PEDESTRIAN CURB RAMP	10.44		440	SF	\$
178	BICYCLE CURB RAMP	10.44		560	SF	\$
179	CONCRETE CURB AND GUTTER	10.44		360	LF	\$
180	CONCRETE CURB	10.44		120	LF	\$
181	MOUNTABLE TRUCK APRON	10.44		90	SF	\$
182	COMMERCIAL DRIVEWAY	10.44		780	SF	\$
183	48" HIGH LANE DELINEATORS	10.66		26	EA	\$
184	NEW SIGNAGE	10.65		11	EA	\$
185	6" DETECTABLE WARNING STRIP	10.44		125	SF	\$
186	TRUNCATED DOMES	10.44		115	SF	\$
187	STRIPING: 24" SOLID WHITE LINE	10.48		1,580	LF	\$
188	STRIPING: 12" SOLID WHITE LINE	10.48		90	LF	\$
189	STRIPING: 4" BROKEN YELLOW LINE	10.48		850	LF	\$
190	STRIPING: 4" BROKEN WHITE LINE	10.48		600	LF	\$
191	STRIPING: 4" SOLID WHITE	10.48		530	LF	\$
192	PAVEMENT MARKINGS	10.48		66	EA	\$

CAT/RAMP + GAP
CIP# 91402

BID SCHEDULE
Page xx

ITEM	DESCRIPTION	SPEC. REF.	UNIT COST	QTY.	UNIT	AMOUNT
193	NON REFLECTIVE MARKERS	10.48		40	EA	\$
194	GREEN THERMOPLASTIC PAVEMENT MARKING	10.48		3,150	SF	\$
195	DRAIN INLETS	10.36		4	EA	\$
196	6" PVC STORM DRAIN PIPE	10.37		120	LF	\$
197	12" RCP STORM DRAIN PIPE	10.37		138	LF	\$
198	ADJUST UTILITY BOX TO GRADE	10.38		2	EA	\$
199	CONNECT TO EXISTING STORM SYSTEM	10.35		3	EA	\$
200	TRAFFIC SIGNAL MODIFICATION (WEBSTER ST/ATLANTIC AVE)	10.50		1	LS	\$
201	TRAFFIC SIGNAL MODIFICATION (ATLANTIC AVE/CONSTITUTION WAY)	10.50		1	LS	\$
FUNDING PACKAGE #5 (CDBG)						
202	ATLANTIC AVENUE RECTANGULAR RAPID FLASHING BEACON (RRFB) ASSEMBLY	10.50		1	LS	\$
203	TRAFFIC SIGNAL MODIFICATION (FIFTH ST/RAMP)	10.50		1	LS	\$

BID ALT #1

204	LIGHT FIXTURE, POLE, AND FOUNDATION	10.81		42	EA	\$
205	1.5" PVC LIGHTING CONDUIT	10.76		4,135	LF	\$
206	LIGHTING IN-GRADE PULL BOX	10.78		42	EA	\$
207	#10 THWN CONDUCTORS	10.76		4,680	LF	\$
208	#8 THWN CONDUCTORS	10.76		22,780	LF	\$
209	TRENCHING	10.77		4,135	LF	\$
210	UTILITY PAD MOUNT	10.80		1	EA	\$

BID ALT #2

211	IMPORT AND PLACE CLEAN FILL	10.28		13,000	CY	\$
-----	-----------------------------	-------	--	--------	----	----

TOTAL BASE BID: Items 1 through 203 inclusive (IN WORDS): \$

TOTAL ADD ALTERNATE BID #1 (IN WORDS): \$

TOTAL ADD ALTERNATE BID #2 (IN WORDS): \$

BIDDER NAME: _____

Refer to Attachment P "Funding Package Exhibit" for breakdown of funding packages.

This Bid Schedule must be completed in ink and must be included with the sealed Bid Proposal. The unit cost for each item must be inclusive of all costs, whether direct or indirect, including profit and overhead. The sum of all amounts entered in the extended total "Amount" column must be identical to the Base Bid price.

ALTERNATE BID ITEMS

If and when Alternate bid items are called for in the Contract Documents, the lowest responsive bid will be determined on the basis of a total lump sum, equal to the sum of the Base Bid Schedule work only, unless otherwise provided in the Notice Inviting Bids. (Note: Bid Alternates will NOT be part of the determination of lowest responsive bids.)

City may elect to include one or more of the Alternate bid items in the Project scope of work. Accordingly, the City reserves the right to hold the Awarded Contractor to its Bid Alternate bids for no less than 90 days from the award of Contract, and each bidder must ensure that each bid item (Base Bid or Alternate) is balanced and contains a proportionate share of profit, overhead and other costs or expenses which will be incurred by the Bidder. The time required for completion of the Alternate bid items has been factored into the Contract Time and no additional time will be allowed for performing any of the alternate bid items.

END BID PROPOSAL

CAT/RAMP + GAP
CIP# 91402


BID SCHEDULE
Page xx

(exhibit from CAT / RAMP + Gap Project Manual

View or Download Bid Documents

VIEW / DOWNLOAD THE CONTRACT DOCUMENTS

Plans and specifications can be obtained from BPXpress Reprographics located at 4903 Central Avenue, Richmond, CA 94804 for a non-refundable cost of \$100.00 per set. Electronic copies of the documents are also available for a non-refundable cost of \$50 per set. Copies of the documents can be viewed and ordered at www.blueprintexpress.com/alameda. They can also be ordered by contacting BPXpress Reprographics by phone at (510) 559-8299 or by email at Richmond@blueprintexpress.com. It is the responsibility of each prospective bidder to confirm his/her firm is on the plan holders list held at BPXpress to ensure receipt of any subsequent communications, such as Addenda.



View or Download Construction Documents

BUILDER'S EXCHANGES (1 of 2)		
<p>Bay Area Builder's Exchange 3055 Alvarado Street San Leandro, CA 94577 Attn: Jan Sanchez Email: planroom@bavareabx.com jeannie@calbx.com Ph: 510-483-8880 Fx: 510-352-1509</p>	<p>Asian Inc. 1167 Mission St. #4 San Francisco, CA 94103-1519 Ph: 415-928-5910</p>	<p>Marin Builders Association 660 Las Gallinas Avenue San Rafael, CA 94903 Attn: Janet Email: kellie@marinba.org Ph: (415) 462-1220 Fx: (415) 462-1225</p>
<p>Sacramento Builders Exchange 1331 "T" St. Sacramento, CA 95814 Attn: James E. Lambert Email: jobdata@sacregionbx.com Ph: (916) 442-8991 Fx: (916) 446-3117</p>	<p>McGraw Hill Construction Dodge 4300 Beltway Place, Suite 180 Arlington, TX 76018 Attn: Char (document coordinator for all Alameda County projects) Ph: (925) 706-6983 (Char's #) Fx: 1-877-836-5711 dodge_reocwe@mcgraw-hill.com</p>	<p>Nor-Cal Bidder's Exchange C/O BPXpress Reprographics 4740 East Second Street, #29 Benicia, CA 94510 Ph: (707) 745-3593 Fax: (707) 745-3595 ncbx@blueprintexpress.com <i>**Prefers electronic files, but file size cannot exceed 15 MB. Larger files have to be mailed, or split into smaller files**</i></p>
<p>Peninsula Builders Exchange 737A Industrial Road San Carlos, CA 94070 Attn: Mickey Email: support@constructionplans.org andrea@constructionplans.org Ph: (650) 591-4486 Fx: (650) 591-8108</p>	<p>Central California Builders Exchange 1244 N. Mariposa St. Fresno, Ca 93703 Email: davia@cencalbx.com Phone (559) 237-1831 Fax (559) 264-2532</p>	<p>San Francisco Builders Exchange 850 So. Van Ness Ave. San Francisco, CA 94110 Attn: Deanna Email: djohnsonsf@sbcglobal.net Ph: (415) 282-8220 Fx: (415) 821-0363</p>

View or Download Construction Documents

BUILDER'S EXCHANGES (2 of 2)		
<p>Contra Costa Builders Exchange 2440 Stanwell Drive Concord, CA 94520 Attn: April Hamilton Ph: (925) 685-8630 Fx: (925) 685-3424 Use: aprilh@ccbxs.com General mailbox: info@ccbxs.com Web: www.ccbxs.com</p>	<p>Reed Construction Data 30 Technology Parkway South, Suite 100 Norcross, GA 30092 Email: jeannie.kwan@reedbusiness.com Ph: (510) 818-0199 Fx: (800) 642-2437 FedEx Acct: 425024124</p>	<p>Builders Exchange of Santa Clara 400 Reed Street PO Box 58032 Santa Clara, CA 95050 Attn: Kanani Email: kf@bxsc.co Ph: 408-727-4000 Fx: 408-727-2779</p>
<p>Valley Builders Exchange 1118 Kansas Ave. Modesto, CA 95351 Ph: (209) 522-9031 Fax: (209) 522-0616 Email: habowden@vallebx.com</p>	<p>Placer County Builders Exchange 10656 Industrial Ave, Suite #160 Roseville, CA 95678 Ph: (916) 771-7729 Fax: (916) 771-0556 planroom@placrbx.com</p>	<p>Solano Napa Builders Exchange 135 Camino Dorado Napa, CA 94558 Attn: Bobbie Email: planroom@snbe.com Ph: (707) 255-2515 Fx: (707) 255-2749</p>
<p>ISQFT Plan Room Plan IT Reprographics 77738 Flora Road Palm Desert, CA 92211 Ph: 1-800-364-2059 ext. 8262 Fax: 1-866-570-8187 Email: content@constructconnect.com EMAIL LARGE FILES TO: sandiegoisqft@gmail.com</p>	<p>Builders Exchange of Stockton, Inc. 7500 West Lane Stockton, CA 95210 Attn: Jeanette Email: jverstl@besonline.com Ph: 209-478-1000 Fx: 209-478-2132</p>	<p>Builders Exchange of Merced & Mariposa 415 West 18th Street, Suite 7 Merced, CA 95340 Ph: 209-722-3612 Fax: 209-722-0207 info@bxmm.org</p>
<p>Construction Bidboard 4420 Hotel Circle Court, Ste. 215 San Diego, CA 92108 Attn: Plan Room Ph: (800) 479-5314 Fx: (619) 688-0585 eplanroom@mediagrif.com</p>	<p>Construction Bid Source P.O. Box 568 Burson, CA 95225-0568 Ph: (209) 772-3670 Fax: (209) 772-3573 (do not fax addendums) *Email Addendums to: projects@constructionbidsource.com</p>	<p>Construction Bid Source 6265 Hwy 9 Felton, CA 95018</p>

Bid Advertisement

City of Alameda



Date: Thursday, August 2, 2018

RE: **Bid Advertisement for Cross Alameda Trail, Ralph Appezzato Memorial Parkway Improvements (aka: CAT / RAMP + Gap, CIP#: 91402)**

NOTICE TO PROPOSERS

Pursuant to City of Alameda Ordinance No. 3154, Section 2-59.2 of the (amended) Alameda Municipal Code, on July 26, 2018, the City Engineer has approved the plans, specifications, and designs for this City Public Works project. The City of Alameda authorized the solicitation of bids for the Cross Alameda Trail, Ralph Appezzato Memorial Parkway Improvements, No. P.W. 03-18-11. **This project is being advertised for bidding on Thursday, August 2, 2018.**

The bid opening date is Thursday, August 30, 2018. All bids are due no later than 2 p.m. to the City Hall West, Public Works Department, Alameda Point, Building 1, 950 West Mall Square, where they will be accepted at Room 110, Alameda, CA 94501. The bid opening time is 2:01 p.m. and will be held at Room 156.

Pursuant to City of Alameda Ordinance No. 3154, Section 2-61.4 of the (amended) Alameda Municipal Code, **Award of Contract to the lowest, responsive, responsible bidder will be by City Council's Authorization, and is presumed to be the evening of Tuesday, October 16, 2018.**

Plans and specifications can be obtained from BPXpress Reprographics located at 4903 Central Avenue, Richmond, CA 94804 for a non-refundable cost of \$100.00 per set. Shipping and handling are extra, depending on the delivery method. Electronic copies of the documents are also available for a non-refundable cost of \$50 per set. Copies of the documents can be viewed and ordered at www.blueprintexpress.com/alameda. They can also be ordered by contacting BPXpress Reprographics by phone at (510) 559-8299 or by email at Richmond@blueprintexpress.com. For any questions about ordering or downloading process, please contact BPXpress. It is the responsibility of each prospective bidder to confirm his/her firm is on the plan holders list held at BPXpress to ensure receipt of any subsequent communications, such as Addenda.

Any Addenda issued before the time in which to submit Bids expires shall form a part of the Contract Documents and shall be included in the Bid. Bidders shall acknowledge and confirm receipt of any and all addenda in their Bid proposals.

City of Alameda



Please note that the Alameda City Council encourages all contractors and other businesses providing services to the City to hire Alameda residents, pursuant to City Resolution No. 12278.

"The City of Alameda is a charter City and any contracts into which the City enters may be subject to the provisions of its charter, which may supersede certain provisions of the Public Contract Code and other provisions of state law".

A mandatory Pre-Bid Meeting will be held at the Public Works Department, 950 W. Mall Square, Conference Room 156, Alameda, CA, 94501, at 10:30 am on Thursday, August 9, 2018. A non-mandatory (optional) Site Walk is offered on the same day at 9:00 a.m. at the Webster St. & Ralph Appezzato Memorial Parkway part of the project site. (Participants to meet just west of the existing bus stop at the far eastern end of the project – SW corner of Webster St. & Ralph Appezzato Memorial Parkway. Site tour expected to be 30 minutes maximum.) 10:30 am Pre-Bid meeting follows, at City Hall West.

Contact Jack Dybas, Project Manager, Alameda Public Works Dept. at (510) 747-7948 or Rochelle Wheeler, Sr. Transportation Planner, Transportation Planning Division, at (510) 747-7442 for more information.

Bid Questions Cut-Off Date

Please submit all Bid Documents' questions by email no later than 3:00 PM Wednesday, August 22, 2018 to:

Jack Dybas, Project Manager, Public Works Department at:

jdybas@alamedaca.gov

and to:

Eric Swanson, Project Manager, BKF Engineers, at:

eswanson@bkf.com

with a copy to:

Rochelle Wheeler, Senior Transportation Coordinator, Transportation Planning Division

at: rwheeler@alamedaca.gov

(City will publish responses to final bid questions 24 hours later, Thursday, August 23.)

(exhibit from CAT / RAMP + Gap Project Manual)

Bid Opening

NOTICE IS HEREBY GIVEN that the City of Alameda will receive sealed bids until 2:00 p.m. on Thursday, August 30, 2018 for the CAT / RAMP + Gap, No. P.W. 03-18-11. Bids to be presented to Jack Dybas, City of Alameda Public Works Department, 950 W. Mall Square, Room 110, Alameda, CA 94501, under sealed cover, marked on the outside: “CITY OF ALAMEDA - SEALED BID for CAT / RAMP + Gap, No. P.W. 03-18-11.” **(Bids will be received and stamped in Room 110, and opened in Room 156.)**

(exhibit from CAT / RAMP + Gap Project Manual

Council Award, Contract Time

**City Council Award of Bid & Contractor Agreement:
Tuesday, October 16, 2018 (estimated).**

**Contract Time is
One Hundred and Forty-Six (146) consecutive working days
from date of Notice to Proceed.
(approximately 7 months)**

Questions

Q & A?

